

# BioMates



Public Summary of Deliverable D 5.6:

Technical risk management report – 2<sup>nd</sup> update

*Version 01*

Grant Agreement number:	727463
Project Acronym:	BioMates
Project title:	Reliable Bio-based Refinery Intermediates — BioMates
Start date of the project:	01.10.2016
Duration of the project:	30.11.2021
Deliverable N°:	D40
Relative Deliverable N°:	D5.6
Work Package N°. Task N°:	WP5 (Task 5.1)
Deliverable title	Technical risk management report– 2 <sup>nd</sup> update
Scheduled date of submission	31/10/2019
Date of submission of Version 01:	29/10/2019
Version:	01
Date of submission of this version:	29/10/2019
Dissemination Level:	Complete deliverable: Confidential, only for members of the consortium (including the Commission Services)
	<b>This summary: Public</b>
Project website address:	<a href="http://www.biomates.eu">www.biomates.eu</a>
The deliverable is elaborated on the basis of	Amendment AMD-727463-21
Submitting party:	CERTH
Responsible author:	Stella Bezergianni
Co- author(s):	Panagiota Manara, Rocio Diaz-Chavez, Yara Evans, Volker Heil, Leonard Raymakers, Luděk Meca, Michael Martin, David Kubička
Reviewer:	
Verification:	Report with public summary

This project has received funding from the European Union's Horizon 2020 research and innovation programme under grant agreement No 727463.



## Contents

1. Introducing BioMates.....	1
1.1. The BioMates Project .....	1
1.2. European Commission support.....	1
1.3. The BioMates team .....	2
2. Preface .....	2
3. Introduction.....	2
4. Technical risks - 2 <sup>nd</sup> update .....	3
5. Health risks management - 2 <sup>nd</sup> update .....	3
6. Process streams quality monitoring - 2 <sup>nd</sup> update .....	4
7. Disclaimer .....	4
8. Literature.....	4

## 1. Introducing BioMates

### 1.1. The BioMates Project

The BioMates project aspires in combining innovative 2<sup>nd</sup> generation biomass conversion technologies for the cost-effective production of *bio*-based intermediates (BioMates) that can be further upgraded in existing oil refineries as renewable and reliable co-feedstocks. The resulting approach will allow minimisation of fossil energy requirements and therefore operating expense, minimization of capital expense as it will partially rely on underlying refinery conversion capacity, and increased bio-content of final transportation fuels.

The BioMates approach encompasses innovative non-food/non-feed biomass conversion technologies, including **ablative fast pyrolysis (AFP)** and single-stage **mild catalytic hydroprocessing (mild-HDT)** as main processes. Fast pyrolysis in-line-catalysis and fine-tuning of BioMates-properties are additional innovative steps that improve the conversion efficiency and cost of BioMates technology, as well as its quality, reliability and competitiveness. Incorporating **electrochemical H<sub>2</sub>-compression** and the state-of-the-art **renewable H<sub>2</sub>-production** technology as well as **optimal energy integration** completes the sustainable technical approach leading to improved sustainability and decreased fossil energy dependency. The overall BioMates-Concept is illustrated in Figure 1.

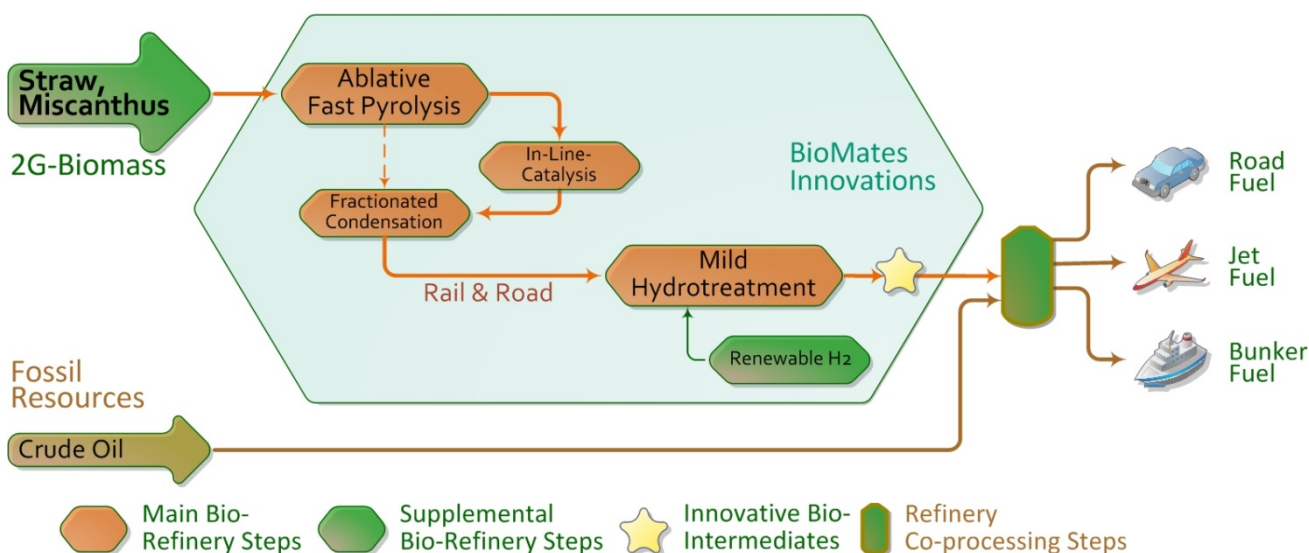


Figure 1: The BioMates-concept

The proposed technology aims to effectively convert residues and non-food/feed plants or commonly referred to as 2<sup>nd</sup> Generation (straw and short rotating coppice like miscanthus) biomass into high-quality bio-based intermediates (BioMates), of compatible characteristics with conventional refinery conversion units, allowing their direct and risk-free integration to any refinery towards the production of hybrid fuels.

### 1.2. European Commission support

The current framework strategy for a Resilient Energy European Union demands energy security and solidarity, a decarbonized economy and a fully-integrated and competitive pan-European energy market, intending to meet the ambitious 2020 and 2030 energy and climate targets /EC-2014a/ EC-2014b/. Towards this goal, the European Commission is supporting the BioMates project for validating the proposed innovative technological pathway, in line with the objectives of the LCE-08-2016-2017 call /EC-2015/. This project has received funding

from the European Union's Horizon 2020 research and innovation programme under grant agreement No 727463.

### 1.3. The BioMates team

The BioMates team comprises eight partners from industry, academia and research centres:

- Fraunhofer Institute for Environmental, Safety, and Energy Technology UMSICHT, Germany (Project Coordination) - [www.umsicht.fraunhofer.de](http://www.umsicht.fraunhofer.de)
- Centre for Research & Technology Hellas / CERTH - Chemical Process & Energy Resources Institute / CPERI, Greece - <http://www.cperi.certh.gr/>
- University of Chemistry and Technology Prague, Czech Republic - <http://www.vscht.cz>
- Imperial College London, United Kingdom  
[www.imperial.ac.uk](http://www.imperial.ac.uk)
- Institut für Energie und Umweltforschung Heidelberg GmbH / ifeu, Germany - [www.ifeu.de](http://www.ifeu.de)
- HyET Hydrogen B.V. / HyET, The Netherlands - [www.hyet.nl](http://www.hyet.nl)
- RANIDO, s.r.o., Czech Republic  
<http://www.ranido.cz/>
- BP Europa SE, Germany  
[www.bp.com/en/bp-europa-se.html](http://www.bp.com/en/bp-europa-se.html)

For additional information and contact details, please visit [www.biomates.eu](http://www.biomates.eu).

## 2. Preface

BioMates Technical Risk Management Reports (TRMRs) provide an overview of the identification and management of the internal risks that arise from within the project as part of Task 5.1 “Management of technical risks, health risks and product quality issues”. The current document, D40/D5.6, entitled “Technical Risk Management Report – 2<sup>nd</sup> update”, is the 2<sup>nd</sup> update of D11/D5.1 “Technical Risk Management Report”. The described internal risks include technical risks, health risks and product quality issues. A brief introduction of the technical/health risks management and process streams quality monitoring targets is initially provided in section 3. In section 4, the registry of the technical risks associated with the project is provided, as a tool of monitoring the technical actions, including means of mitigating these risks. Unforeseen risks have been also registered. An update of the health risks management related with the project is presented in section 5. Finally, the process streams (feedstocks, products, catalysts) quality monitoring approach is presented in section 6.

## 3. Introduction

BioMates project involves several innovative processes and streams, as described in section 1, that are strongly interlinked, rendering essential to define a comprehensive and consistent approach to monitor the technical activities while minimizing the likelihood of problems during the different stages of project execution. The technical assessment is continuously performed as already presented in Deliverable D8.3 “1<sup>st</sup> Technical Assessment report” submitted in September 2017 and its update D8.6 “2<sup>nd</sup> Technical Assessment report”. However, the risk management involving technical and health internal risks during project execution and streams quality monitoring will be presented in the Technical risk management reports. Therefore, the current document, D40/D5.6, entitled “Technical Risk Management Report – 2<sup>nd</sup> update”, is the 2<sup>nd</sup> update of D11/D5.1 “Technical Risk Management Report”. In particular, the first delivered Technical Risk Management

Report (TRMR1) corresponds to the period October 2016 (M01) to October 2017 (M13), the “Technical Risk Management Report-1<sup>st</sup> update” (TRMR2) is related to the period between November 2017 (M014) and October 2018 (M25), while, the “Technical Risk Management Report-2<sup>nd</sup> update” (TRMR3) addresses the period between November 2018 (M26) and October 2019 (M38).

#### 4. Technical risks - 2<sup>nd</sup> update

The BioMates project encompasses two main innovative non-food/feed biomass conversion technologies, ablative fast pyrolysis (AFP) and single-stage mild catalytic hydrotreatment (mild-HDT). Each of these main biomass conversion technologies have individual innovative components such as in-line catalysis and fractionation condensation integrated with AFP, and tailor-made catalyst development and electrochemical hydrogen compressor and pumping integrated with mild-HDT. All the aforementioned technologies, that are combined to develop in TRL3 and to validate in an industrially relevant environment TRL5 a new biomass-to-biofuel production pathway, are strongly interlinked and as a result thus render certain technical risks related with the well-defined project actions.

The technical risks identified enable project monitoring of the technical actions by tracking their progress and providing appropriate level of contingency planning to address any risks associated with them. The technical risks, the likelihood of their occurrence and severity are juxtaposed with the actions for mitigating them. It should be noted that the list of technical risks is reviewed by the technical manager and the WP1, 2 and 3 leaders every six months, based on the progress of the technical actions of the project. Therefore, unforeseen risks during TRMR1 have been also registered, while monitoring results of the identified risks are provided for both foreseen and unforeseen risks.

#### 5. Health risks management - 2<sup>nd</sup> update

There is a general typology of risk assessment including Human Health Risk Assessment, Ecological Risk Assessment and Applied Industrial Risk Assessment /EEA-2016/. The Applied industrial applications look at real situations and tend to include engineering risk assessments as part of the overall environmental risk assessments with an integrated approach to human and environmental risks /EEA-2016/. This is more related to risk management decisions intended to protect humans and the environment (and the company) within defined spatial boundaries. The health risk assessment in this project has this focus on the risk management according to the risks identified and the end product and involves risk analysis, risk assessment and risk control practices /EEA-2016/.

The Health assessment in the BioMates project involves the handling of the products and their potential impact on humans as well as the process that are taken place within the project. These are aligned with the D 9.1: EPQ - Requirement No. 1 pa BSI - British Standard Institutions, Occupational health and safety management systems — Guide, BS 8800, 2004 /BSI-2004/, particularly on the transport and handling of the pyrolysis bio-oil. It also includes the Health and Safety measures and policies at each one of the institutions partners of the project. Therefore this includes the risk for workers and occupational hazards.

For the general public the health assessment risk is centered on the handling and transport of the Bio-oil.

The health risk assessment will identify criteria on health following the three main steps of risk management: risk analysis, risk assessment and risk evaluation.

## 6. Process streams quality monitoring - 2<sup>nd</sup> update

The BioMates project incorporates several feedstocks, products and other auxiliary streams such as catalysts, the quality and consistency of which is of outmost importance for the project execution and risk minimization. As a result, the consortium of BioMates project has agreed upon the analytical methods for characterizing the process streams, based on which some standards are starting to be developed.

Firstly, the quality of the raw materials used, i.e. the non-food/feed biomass should be defined, as it affects the downstream processing via AFP. Moreover, it is essential to define an analytical basis for the product of AFP (bio-oil) and for the final product of upgrading bio-oil via mild-HDT (BioMates). This analytical basis is employed for evaluating the efficiency of the mild-HDT conversion step as well as the project main product (BioMates). Monitoring analytical results are included in the associated BioMates deliverables (D19/D1.4 “Report on analytics of feedstock, in-line catalysts and AFP bio-oils”; D07/D1.2 “Development of custom made hydrotreating catalyst”; D2.6/D30 “Report on optimal mild-HDT operation of AFP bio-oil upgrading”-upcoming).

## 7. Disclaimer

This Deliverable report reflects only the authors’ view; the European Commission and its responsible executive agency INEA are not responsible for any use that may be made of the information it contains.

## 8. Literature

- BSI-2004 British Standard Institutions, Occupational health and safety management systems — Guide, BS 8800
- EC-2014a European Commission, Communication from the Commission to the European Parliament, the Council, the European Economic and Social Committee and the Committee of the Regions - A policy framework for climate and energy in the period from 2020 to 2030, COM (2014) 15 final, Brussels, 22.1.2014, [http://www.europarl.europa.eu/meetdocs/2009\\_2014/documents/nest/dv/depa\\_20140212\\_06/depa\\_20140212\\_06en.pdf](http://www.europarl.europa.eu/meetdocs/2009_2014/documents/nest/dv/depa_20140212_06/depa_20140212_06en.pdf); <http://bit.ly/1LUcJKL>
- EC-2014b European Commission, Energy Union Package - Communication from the Commission to the European Parliament, the Council, the European Economic and Social Committee and the Committee of the Regions and the European Investment Bank - A Framework Strategy for a Resilient Energy Union with a Forward-Looking Climate Change Policy, COM(2015) 80 final, Brussels, 22.1.2014, [http://eur-lex.europa.eu/resource.html?uri=cellar:1bd46c90-bdd4-11e4-bbe1-01aa75ed71a1.0001.03/DOC\\_1&format=PDF](http://eur-lex.europa.eu/resource.html?uri=cellar:1bd46c90-bdd4-11e4-bbe1-01aa75ed71a1.0001.03/DOC_1&format=PDF), <http://bit.ly/198SAUf>
- EC-2015 European Commission, LCE-08-2016-2017 “Development of next generation biofuel technologies”, Publication date: 14 October 2015, <https://ec.europa.eu/research/participants/portal/desktop/en/opportunities/h2020/topics/lce-08-2016-2017.html>, <http://bit.ly/2ndtvPc>
- EEA-2016 Health Risk Assessment. Chapter 5. <https://www.eea.europa.eu/publications/GH-07-97-595-EN-C2/chapter5h.html> Accessed October 2017
